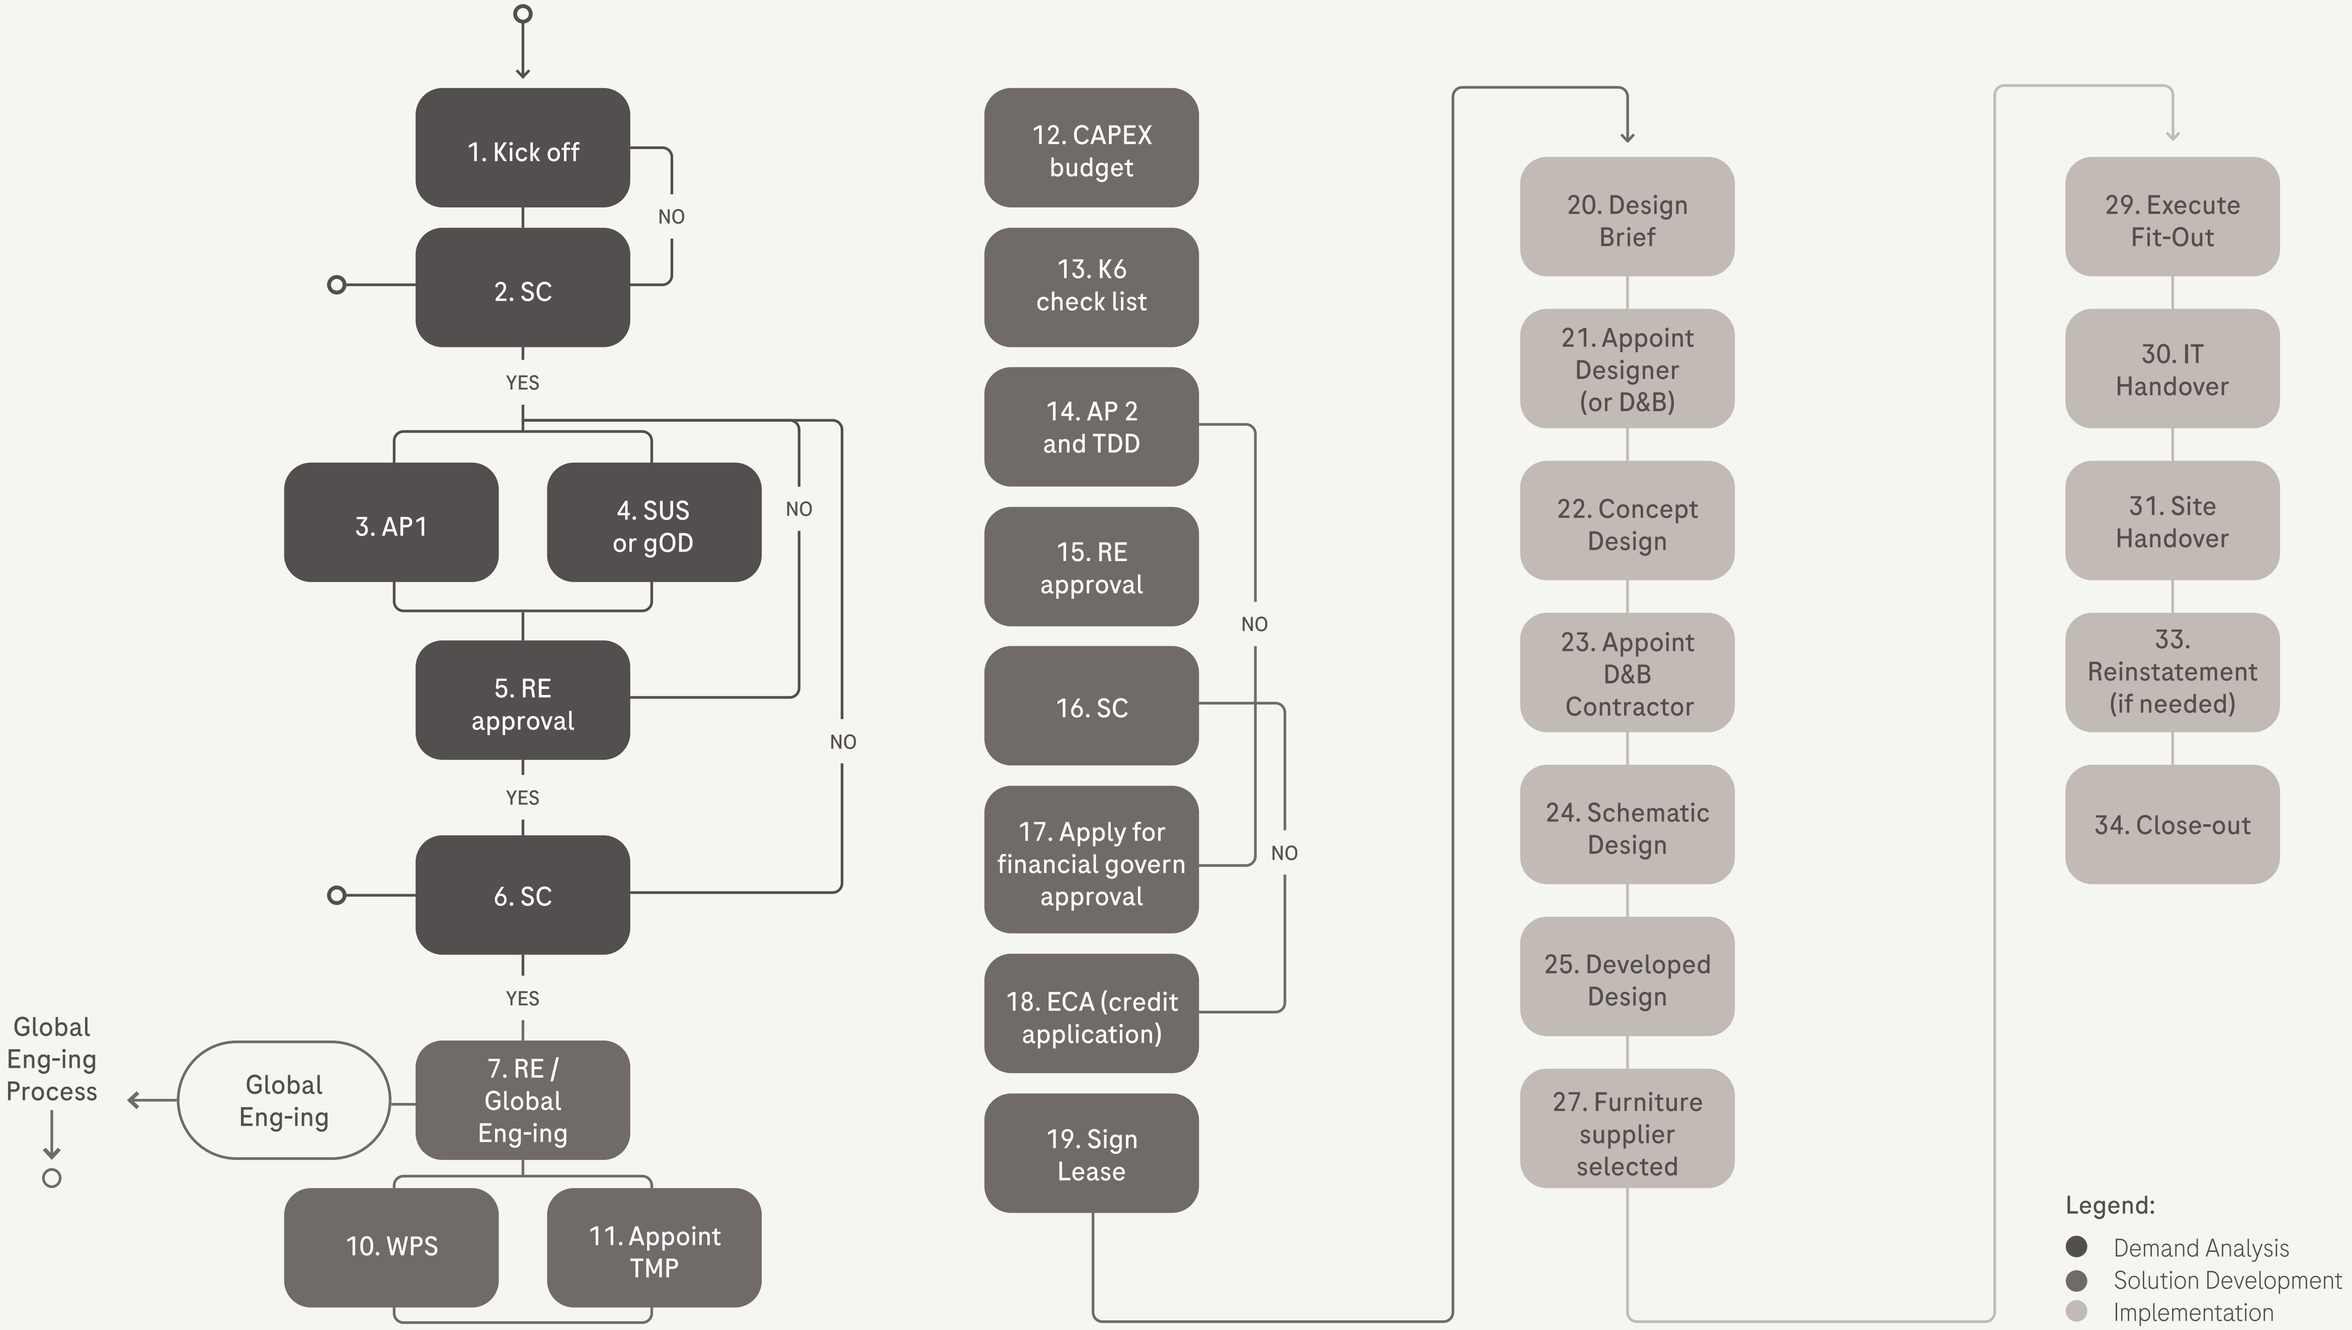
1. Kick off
NO
2. SC
YES
3. AP1
4. SUS or gOD
NO
5. RE approval
NO
YES
6. SC
YES
7. RE / Global Eng-ing
Global Eng-ing
Global Eng-ing Process
10. WPS
11. Appoint TMP
12. CAPEX budget
13. K6 check list
14. AP 2 and TDD
15. RE approval
NO
16. SC
17. Apply for financial govern approval
NO
18. ECA (credit application)
19. Sign Lease
20. Design Brief
21. Appoint Designer (or D&B)
22. Concept Design
23. Appoint D&B Contractor
24. Schematic Design
25. Developed Design
27. Furniture supplier selected
29. Execute Fit-Out
30. IT Handover
31. Site Handover
33. Reinstatement (if needed)
34. Close-out
Legend:
Demand Analysis
Solution Development
Implementation
